

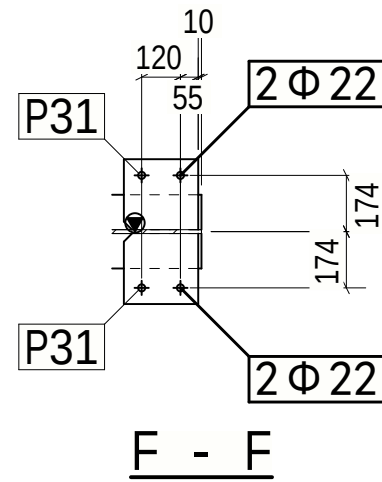
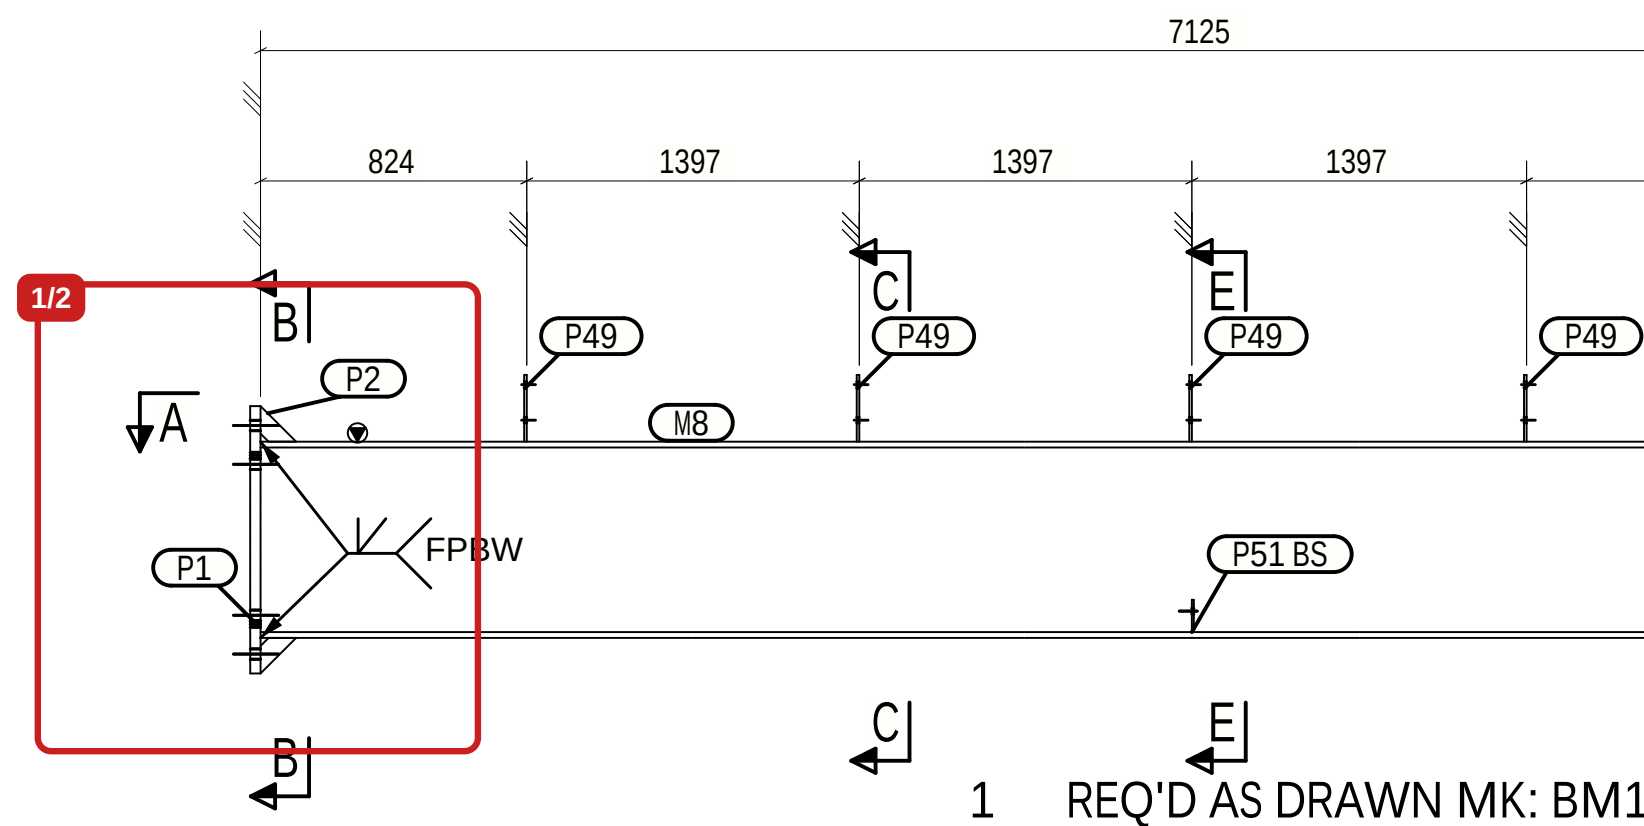


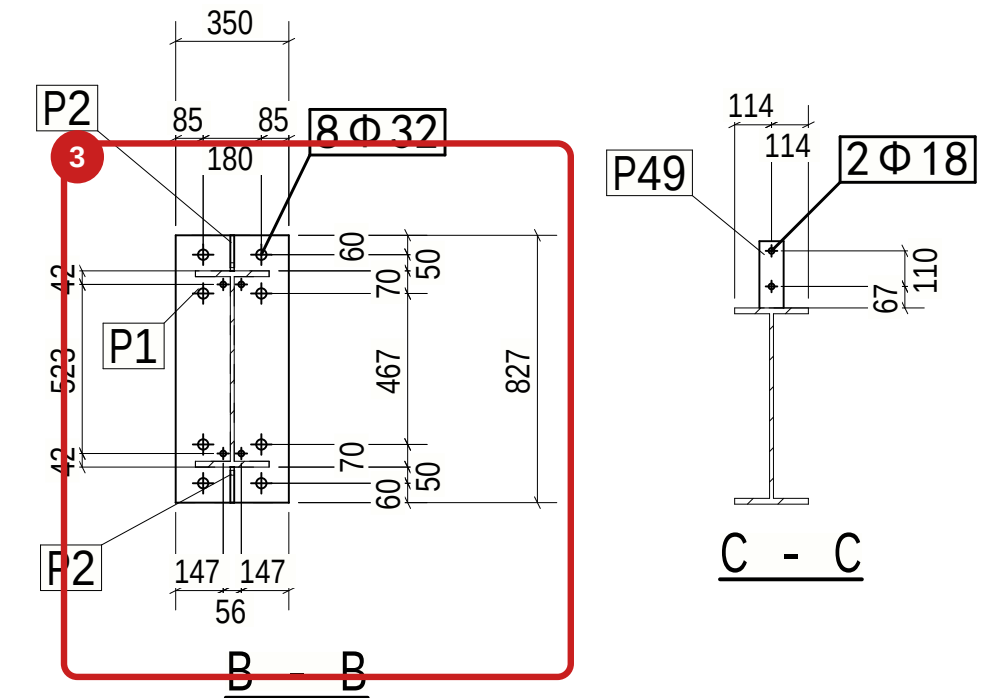


Totals for ONE assembly		947.5
Combined Total for Assembly of	1	947.5

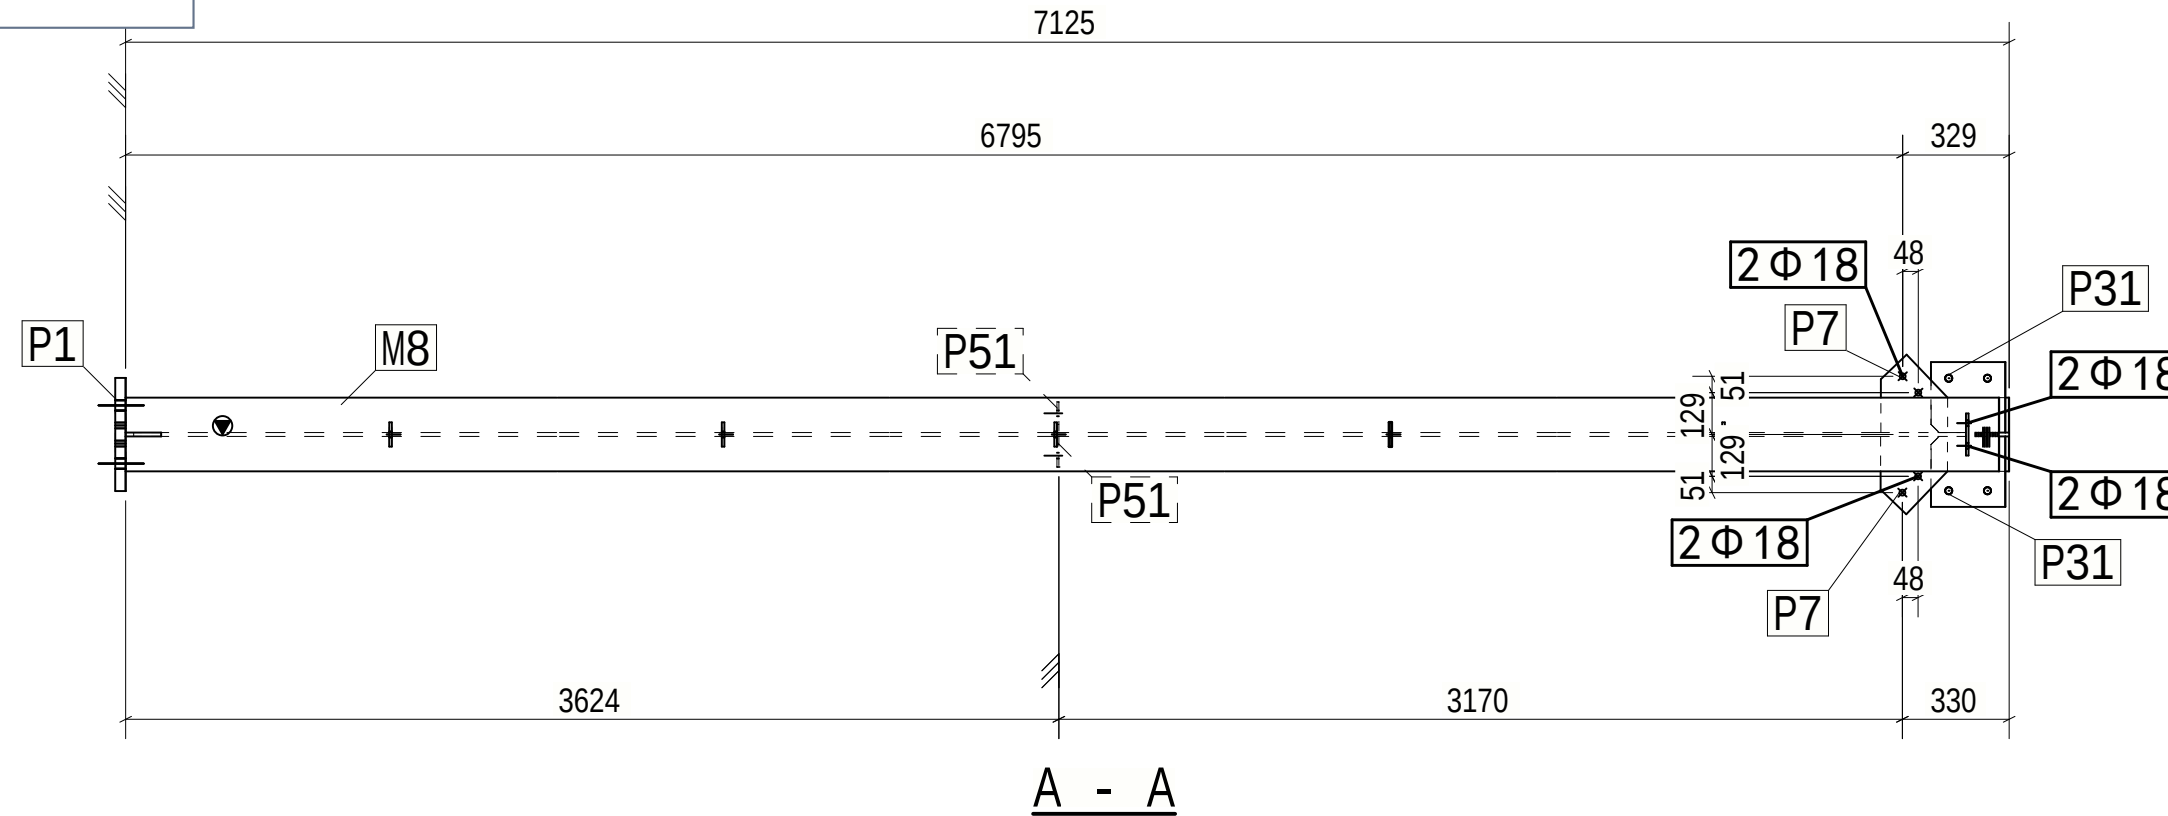

1 REQ'D AS DRAWN MK: BM1

1. Consultant R2 requires PRESET 100 mm; no direction, datum or verification is shown.
2. Consultant S5.0 requires 8 CFW TO WEB; BM1 only shows the general 6 CFW U.N.O. note.
3. P1 Part: 32 hole centre is 60 mm from plate edge, giving 44 mm edge distance; required minimum is 48 mm.

Bolt report cross-check: BM1-BM103 | 8 x M30 HS8.8, 120 long | RP9 matched.

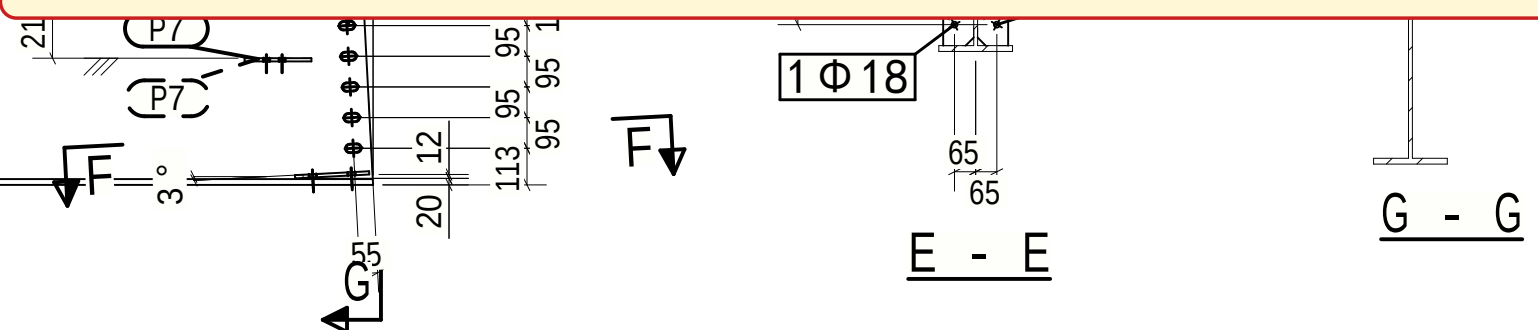

GENERAL NOTES

1. MARK TO BE STAMPED ON TOP FACE WHERE INDICATED
2. STEEL FABR. & CONST. IN ACCORDANCE W/ AS/NZS 5131
3. HOLES SHALL BE 22 U.N.O
4. ALL SNIPES TO BE 15x15 U.O.N.
5. ALL NOTCHES SHALL HAVE 11mm RAD AT INSIDE CORNER
6. ALL WELDS TO BE STRUCTURAL PURPOSE, 6mm CFW U.N.O.
7. WELD TO BE PERFORMED IN ACCORDANCE W/ AS/NZS 1554
8. FABRICATION TOLERANCE -2/+0



STEEL
MINING COMPANY PTY LTD



Project No.
MSC-J-239

DO NOT SCALE - IF IN DOUBT ASK

BM1

B
